

# BOND UPDATE #179

**10.28.22**

Here's what is going on with our bond projects.

Enjoy!

Kristi

1. Work on the FHS campus has continued to progress during the past week. Some of the highlights are outlined below:

## Auxiliary Gym and Kitchen

- The Auxiliary Gym received its occupancy inspection this week and will be turned over for use by the school this coming Monday, Oct. 31. Another milestone hit by our contractors!
- Crews are now installing sheetrock in the kitchen area and preparing for wall paint. While this has been occurring, the kitchen hoods that will exhaust the cooking line are being installed as well.

## Academic Wing & Commons


- The first floor is now completely into the final finishes:
  - Carpet installation is ongoing and should be wrapped up around Nov. 4.
  - Work on the final door hardware, and door painting, is ongoing and should wrap up in the next couple of weeks.
  - Now that a lot of carpet has been installed on this floor, crews are installing baseboard and making good progress.
  - Final clean up on this floor should get started over the next week or two.
- The second floor is transitioning into final finishes:
  - The final ceiling tiles on this floor are now substantially complete.
  - Grinding and polishing work on the corridor floors has made its way this week across half of the second floor. The rest of the floor should be complete in about a week and a half.
  - The carpet on this floor should begin installation over the next couple weeks.
  - Tackable wall coverings are now substantially complete on this floor.
- The third floor is seeing the following activities:
  - Final bathroom accessories are being installed.
  - Tackable wall coverings are being placed on the walls across this floor.
  - Final ceiling tile installation is ongoing.

### CTE Village



- The Agricultural Science Building will have the final electrical and plumbing items placed in the walls, and should be ready for sheetrock & plywood, next week.
- The Aquaculture Building heating equipment installation is complete and plumbing and electrical should be completed over the next couple of weeks.

### Site Work

- The contractors are now setting their sights on the old Aquaculture Building. Demolition of this structure will begin next week. Once it's gone, the generator area can be constructed.
2. At the end of this week's update, you will find several photos of the Ferndale High School site with captions. You can also find more photos on the district website – including daytime pictures of construction taken every two hours, every day – at the following link: [Bond 2019 - Ferndale School District \(ferndalesd.org\)](http://ferndalesd.org)
  3. Below is the FHS project timeline as of August 31. It shows how much of our bond funding we have spent so far and how far along we are in building the new campus.

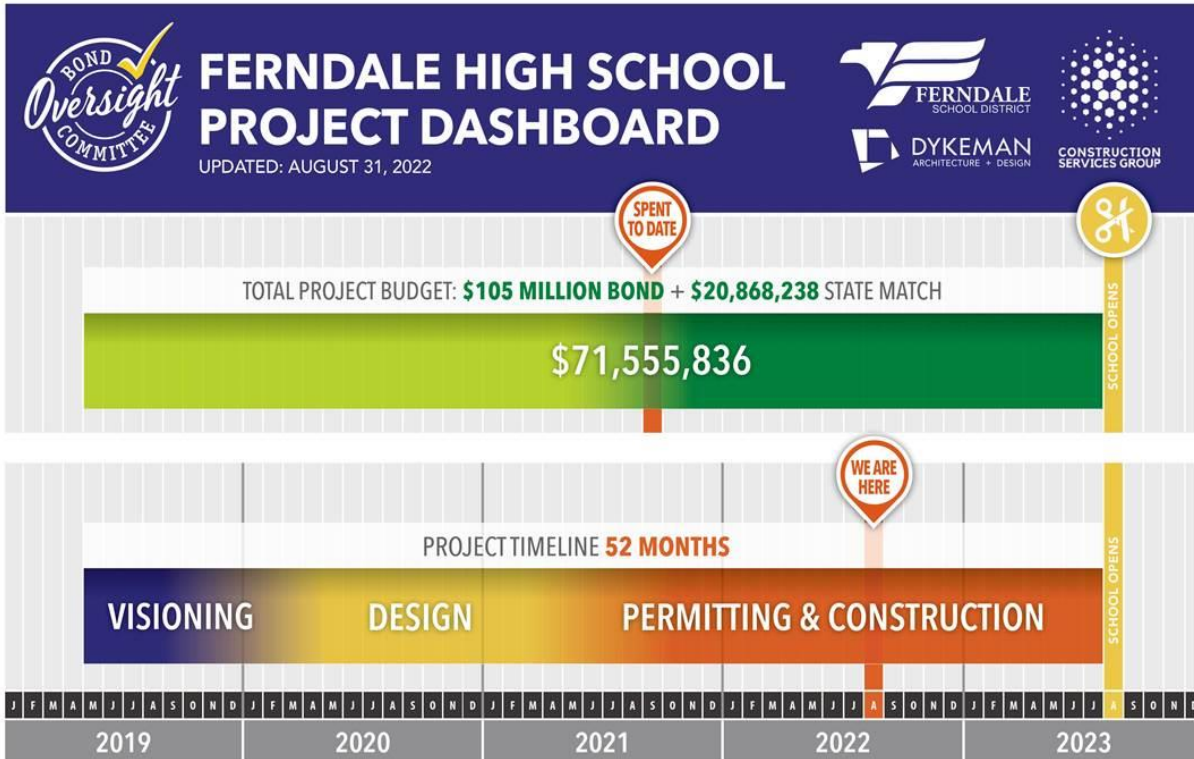

- Below is a map showing the various components of the new FHS campus and when they'll be completed.

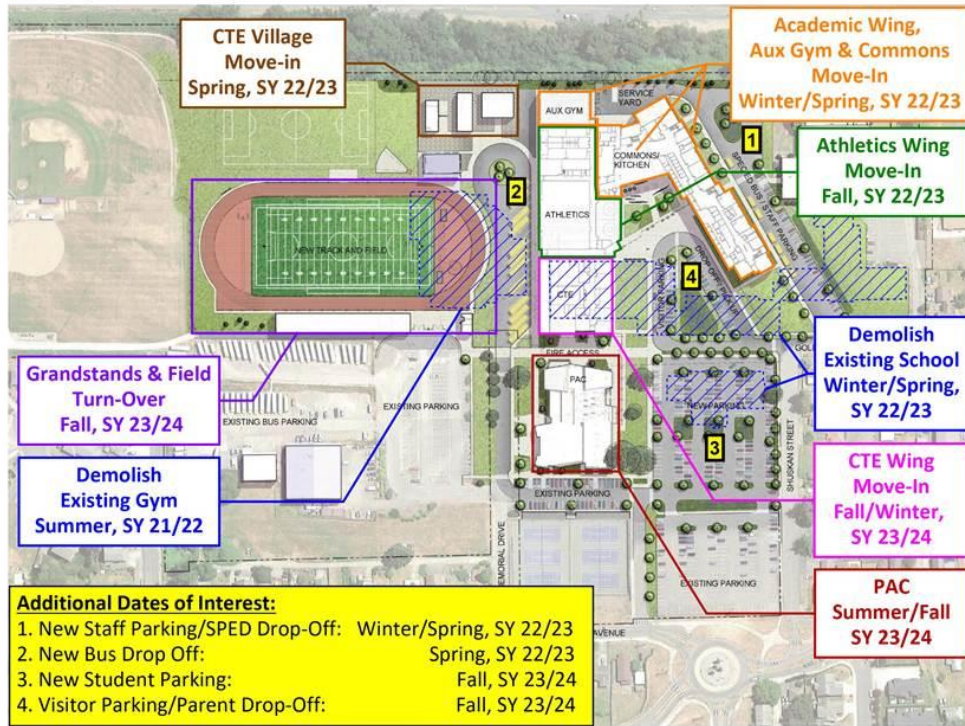

# FHS Move-In Plan

If you have questions or comments about any of the content of this update, please feel free to reach out to me or one of my colleagues.

Kristi





**Finishing touches in the Auxiliary Gym**



**Cooking line pre-manufactured wall being installed in the main kitchen.**

**Sheetrock is also underway.**



**Vinyl flooring in a science room**





**Grinding and polishing of concrete corridor floors in the Academic Wing**





**Final removal of the old greenhouse foundation. Aquaculture demolition starts next week!**
