

BOND UPDATE #181

11.11.22

Here's what is going on with our bond projects.

Enjoy!

Kristi

1. Work on the FHS campus has continued to progress during the past week. Some of the highlights are outlined below:

Kitchen and Common Area

- The kitchen hoods and ceiling grid are complete. Crews will now begin installing fiber-reinforced plastic sheets on many of the walls. These sheets will safeguard the walls from the heat and moisture that is produced by a commercial kitchen.
- Bench stairs are being framed in the Common Area, which will create a gathering point for students and staff. The benches in this area will be capped with reclaimed wood from the old gym floor.

Academic Wing & Commons

- The first floor is now down to the final touches:
 - Final finished painting work is close to wrapping up, and should be complete around the end of next week.
 - The last baseboard installation is making good progress and should be nearly finished in a week and a half.
 - Fire door installation should be done by the end of November.
 - And last but not least, final cleaning is underway.
- The second floor is completely into final finishes:
 - Grinding and polishing of the corridor floors is now complete.
 - Carpet installation is making good progress and should be finished next week.
 - Final baseboard and painting work are ongoing and should be finished by the end of the month.
- The third floor is seeing the following activities:
 - Final bathroom accessories are making good progress and are close to wrapping up.
 - Tackable wall coverings were finished this week.

- Final ceiling tile installation is ongoing and making good progress.
- Corridors are fairly complete and crews are now working on the classrooms.

-

CTE Village


- The sidewalks around the Agriculture Building are now being poured, getting the area closer to a finished state.
- Plywood is being installed on the walls of the Aquaculture Building.

Site Work


- Prep work for the new emergency generator began with underground electrical installation. The next step will be pouring the concrete slab that the generator will sit on.
- Construction of the concrete footings in the courtyard in front of the commons area has begun.
- Crews have now restarted work in the Grandstand area, forming the north-end retaining wall around the high jump area.

2. At the end of this week's update, you will find several photos of the Ferndale High School site with captions. You can also find more photos on the district website – including daytime pictures of construction taken every two hours, every day – at the following link: [Bond 2019 - Ferndale School District \(ferndalesd.org\)](http://ferndalesd.org/Bond2019)

3. Below is the FHS project timeline as of August 31. It shows how much of our bond funding we have spent so far and how far along we are in building the new campus.

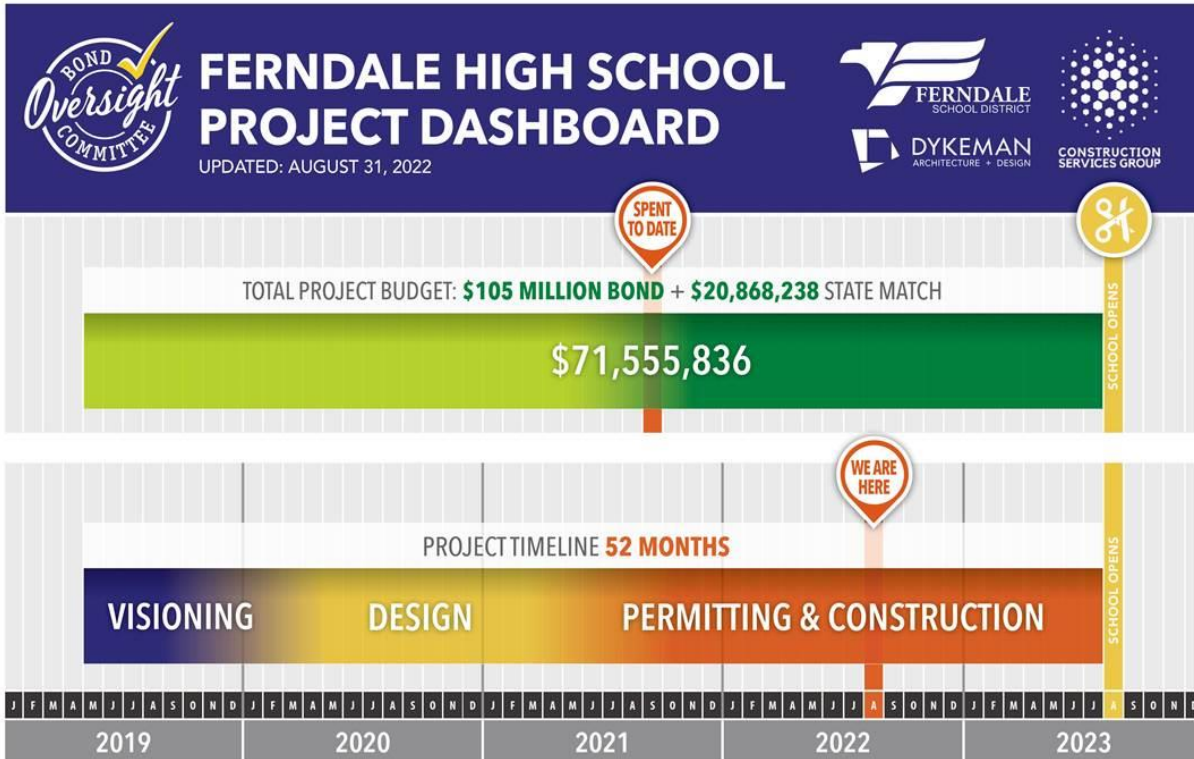

- Below is a map showing the various components of the new FHS campus and when they'll be completed.

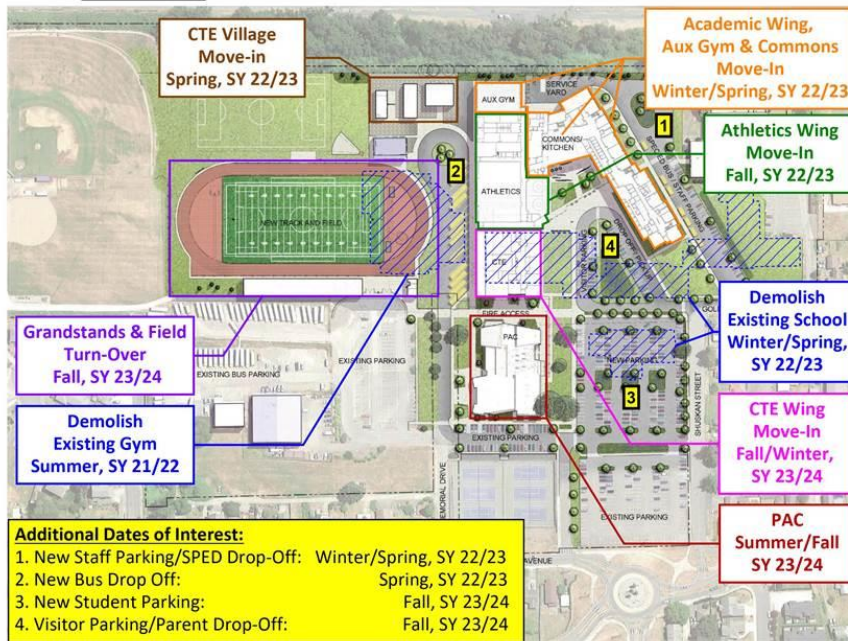

FHS Move-In Plan

If you have questions or comments about any of the content of this update, please feel free to reach out to me or one of my colleagues.

Kristi



Cooking line, exhaust hoods and ceiling grid installation in the kitchen



Canopy footings underway in the courtyard



Common Area gathering benches and stairs being installed



Wood ceiling installation in the library



Carpet installation in a second floor classroom



Concrete slabs being poured around the Agriculture Science Building
