


# BOND UPDATE #187

## 1.13.23



Here's what is going on with our bond projects.

Enjoy!  
Kristi

1. Our new Academic Wing is receiving some finishing touches, including final adjustments to building systems like lighting, heating, communications, security, and more. Now that school is back in session, most of this work is occurring in the evenings after students and staff have left for the day.
2. Hazardous materials are being removed in the north end of the old building this week. This area is being cleared first, so crews can start construction of the new CTE Wing, which will be located just south of the new Athletic Wing. Crews will begin dismantling the old FHS building on the afternoon of Wednesday, Jan. 18, after some safety briefings and an orientation of the area and existing utilities.
3. Crews are hard at work framing the concessions and restroom areas underneath the football field grandstands. Mechanical and electrical installation in that area will start soon, as well as the masonry that will form the exterior walls. Crews continue to pour concrete in the football field area, along with the weight room and new CTE Village areas.
4. Final touches are now underway on the CTE Village. These areas will be turned over for school use soon!
5. Framing work on the greenhouse has resumed in preparation for the new plexiglass panels, which are scheduled to arrive soon. It's very exciting to know this structure has now been recycled for the second time. Originally, the greenhouse structure was donated to the school, and now it has been re-assembled in its third location.
6. Now that the school has turned over the old building footprint, utilities such as natural gas are being extended through those areas.
7. At the moment, final planning preparations are being made for the work that will occur in the Performing Arts Center later this year.
8. At the end of this week's update, you will find several photos of the Ferndale High School site with captions. You can also find more photos on the district website – including daytime pictures of construction taken every two hours, every day – at the following link: [Bond 2019 - Ferndale School District \(ferndalesd.org\)](https://ferndalesd.org)
9. Below is the FHS project timeline as of October 31. It shows how much of our bond funding we have spent so far and how far along we are in building the new campus.

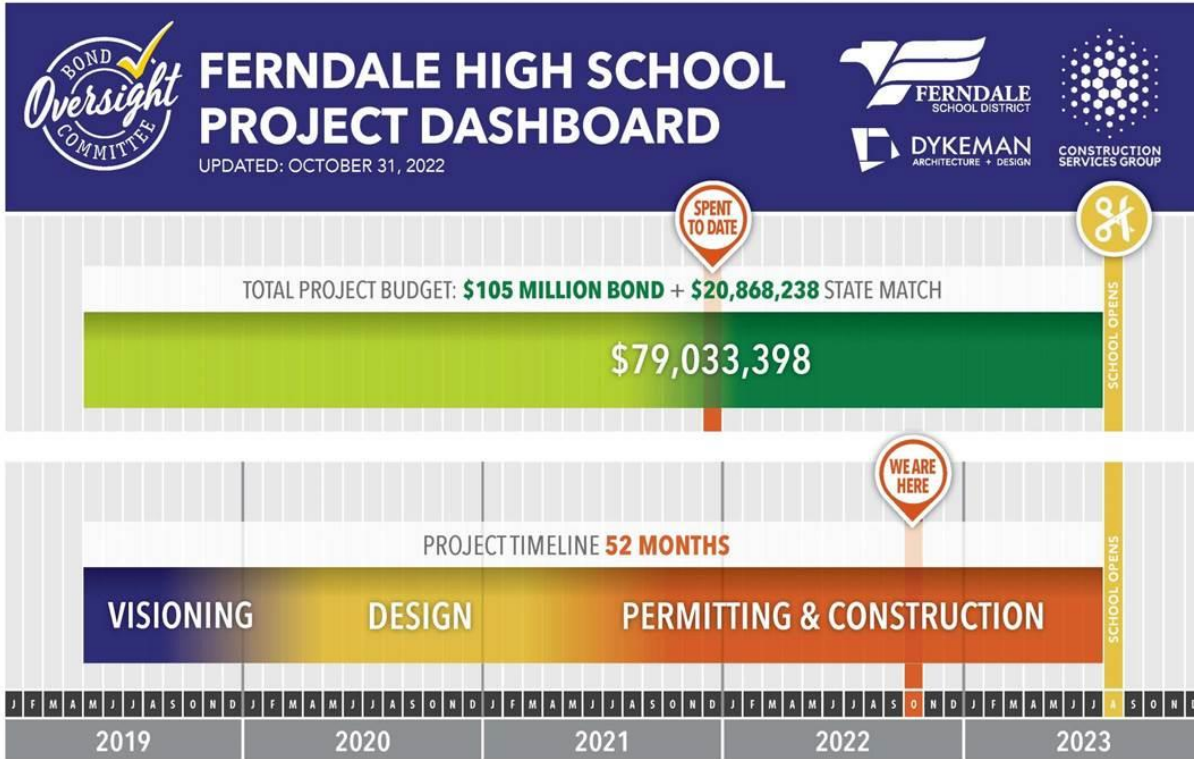

10. Below is a map showing the various components of the new FHS campus and when they'll be completed.

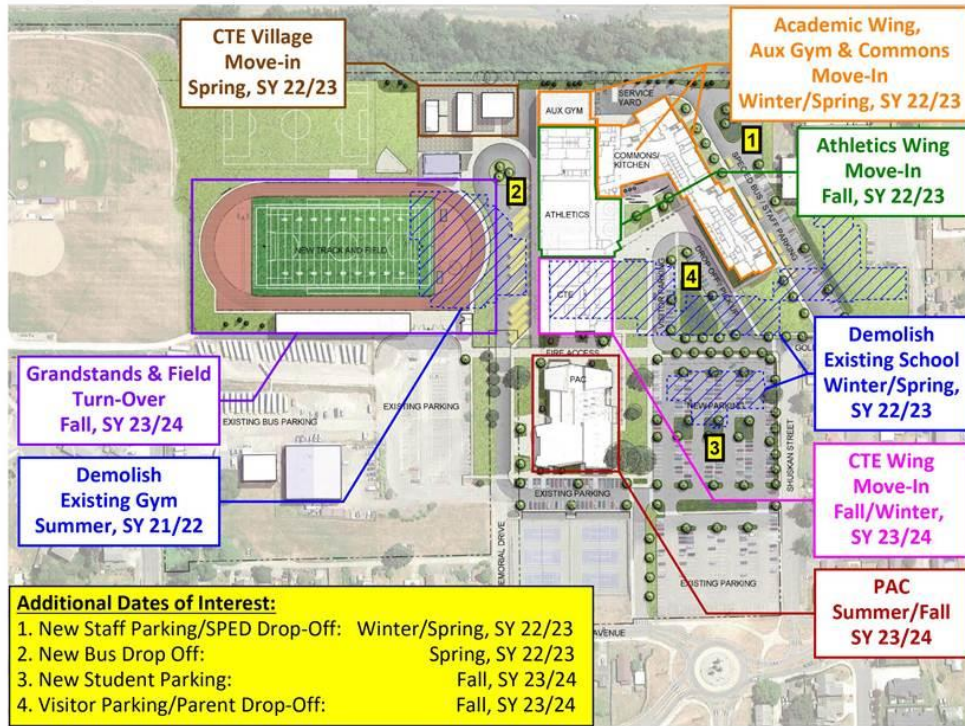

# FHS Move-In Plan

If you have questions or comments about any of the content of this update, please feel free to reach out to me or one of my colleagues.

Kristi



**Framing of the football field grandstand restrooms and concessions area**





**Excavations for the ramp connecting the varying levels of the football field and existing weight room areas**



**Natural gas installation adjacent to the Performing Arts Center**



**Framing work on the greenhouse has now resumed in preparation for the new plexiglass panels coming soon**
